


67 Hunt Street, Suite 119
Agawam, MA 01001
www.cplusa.com

MAIN +1 413 592 0030
FAX +1 413 285 8592



July 2, 2020

City of Easthampton
School Building Committee
Tom Brown, Chairman
50 Payson Avenue
Easthampton, MA 01027

Subject: Maple Elementary – Middle School Project
Weekly Field Report for week of: 6/29/20

Dear Mr. Brown:

Please find attached, the Weekly Field Report for the week of June 29, 2020 for the Maple Elementary / Middle School Project.

If you have any questions, please do not hesitate to contact me.

Regards,

Matt Dunn
Construction Representative

Attachment: Photos
cc: See e mail Distribution List

**MAPLE ELEMENTARY – MIDDLE SCHOOL
REPORT FOR THE WEEK OF: June 29, 2020**

ACTIVITIES WORKED-ON THIS WEEK

- Installation of loop road water main.
- Detailing of Building A steel and galvanized platforms.
- Erected columns in Building D.
- Poured third floor Building B slab on deck.
- Working on Building B roof parapet.
- Completed under-ground Plumbing & Electrical in Bldg. B.
- Finish-graded and compacted Building B slab-on-grade.
- Placed electrical duct-bank conduit along new access road.


ACTIVITIES IN PROCESS	NEXT ACTION	NOTES
Building A & C – detailing & decking Building D – steel erection.	On-going	
Loop road watermain installation.	On-going	
Underground Plumbing and Electrical in Building C.	On-going	
Continuation of electric and telephone duct-bank from roundabout.	On-going	
Preparation for pouring slab-on-grade in Building B.	On-going	



BUNDLES OF STEGO SLAB VAPOR BARRIER FILM



BUILDING A ROOF JOISTS

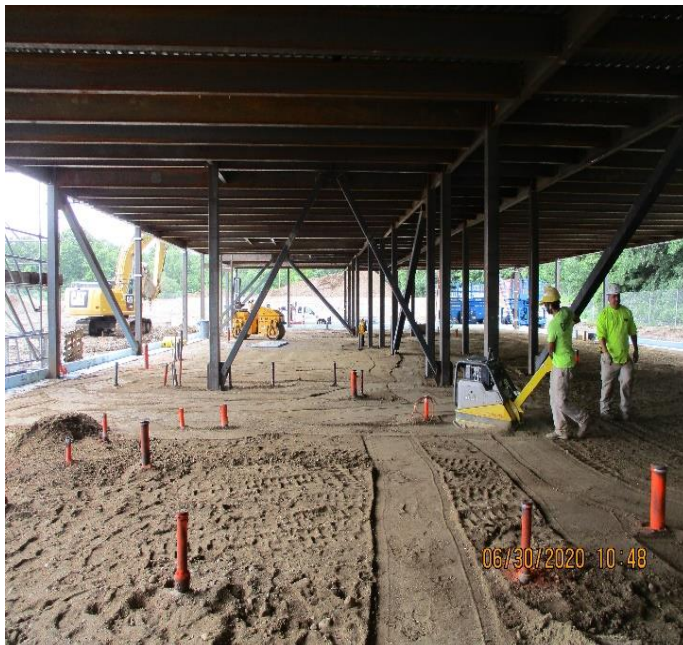

COMPACTION OF BUILDING B SUBGRADE



PERIMETER INSULATION

